


FACTS AND FIGURES

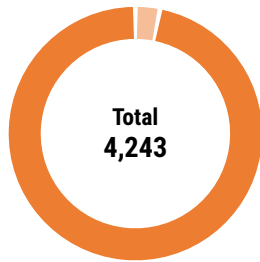

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	96.89%	89.07%
Adobe Structures	1.01%	4.25%
Brick and Cement Mortar Masonry	0.68%	2.11%
Stone and Cement Mortar Masonry	0.61%	0.64%
Others	0.80%	3.93%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	4,528
PA Agreement	4,283 (245)
I st Tranche received	4,283 (245)
II nd Tranche received	3,768 (760)
III rd Tranche received	2,693 (1,835)

Houses

Under Construction: - Completed: 2,918

Retrofitting Status

Total Eligible HHs	96
PA Agreement	6 (90)
I st Tranche received	6 (90)
II nd Tranche received	- (96)

Grievances

Registered: 910
 Addressed: 534

Non-compliances

Registered: -
 Addressed: -

Data Updated on: 2019-05-27 00:00:00

PO Presence

Active: MI (Livelihood), MI (Hygiene), RoomTR (Education)

Phased Out: ACF (Health), ACF (Shelter), CNF (Education), GIZ (Health), MI (DRM), MI (Shelter), MI (Hygiene), OXFAM-GB (Shelter), PA (Shelter), RoomTR (Education)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	78,562	Y	7,000
Aggregate	m ³	79,529	Y	12,000
Sand	m ³	8,380	N	8,000
Timber	cu. ft.	9,640	Y	4,000
Cement (PPC)	Sack	-	Y	850
Cement (OPC)	Sack	264,744	Y	950
Rebars	kgs.	854,640	N	98
Tin	bundle	10,825	-	-
Bricks	pcs.	1,016,100	Y	15

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,500 /-
 1,000 /-

OTHER SECTORS



Schools

Damaged: 38
 Under Construction: 17
 Construction Completed: 17



Health Posts

Damaged: -
 Under Construction: -
 Construction Completed: -

KEY CONTACTS

Municipal Office

Tej Bahadur Tamang
 Mayor
 9841867429

Municipal Office

Jagan Adhikari
 Focal Person
 9841032725

Municipal Office

Sita Khadka
 Deputy Mayor
 9841829147

GMaLI/NRA

Bickey Lakha
 NRA Chief-District
 9849179333

Municipal Office

Narersh Pudasaini
 Administration Officer
 9851230141

DLPIU-Building

Koshnath Adhikari
 DUDBC.DLPIU Chief
 98550465884

HHs WITH LAND ISSUES




STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)



Source: HRRP Analysis

TA ACTIVITIES MAP

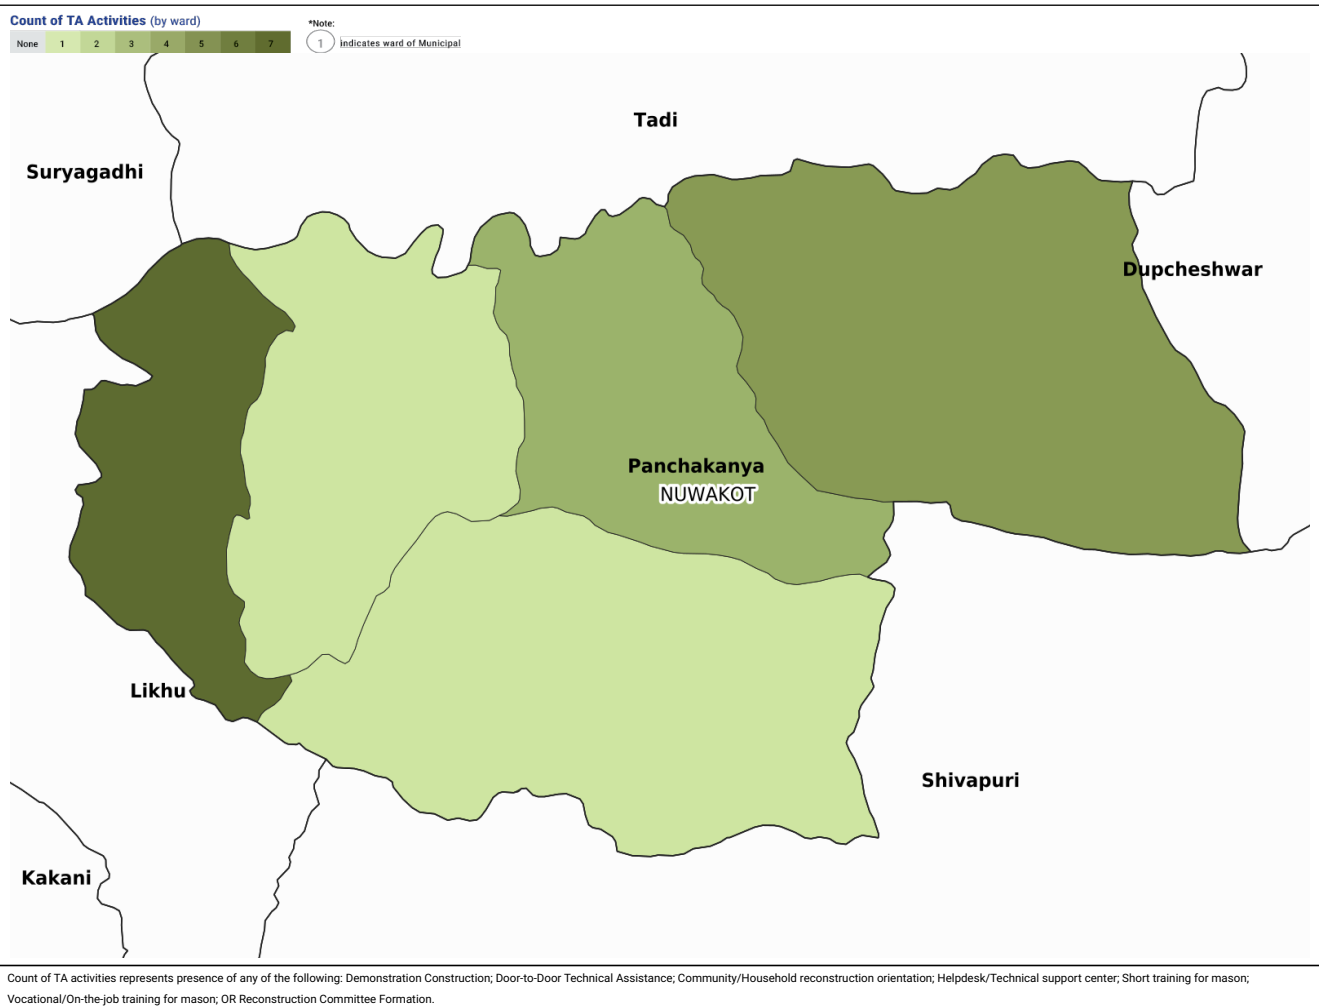

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Badri Pyakurel (District Coordinator) 9851154201	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
